

አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

ISSUE HISTORY			
Issue No	Description of Change	Originator	Effective Date
1	Initial release	Task Force	01 May 2019

REFERENCE DOCUMENTS	
Document Number	Document Title
ES- ISO 9001:2015	Quality Management system-Requirements, clause 8.5
ES-ISO 9000:2005	Quality Management system fundamental and vocabulary
	General & specific condition of contract

CONTENTS	Page No.	FOR DOCUMENT CONTROL USE ONLY
1. Purpose	1	
2. Scope	1	
3. Process Owner	2	
4. Definitions and Abbreviations	2	
5. procedure	3-5	
6. Records	6	
7. Related documents	6	

1. Purpose

To prepare payment certificates and collections.

2. Scope

This procedure is applied by Project manager /Construction Department of ASER construction for payment certificate preparation & payment collection.

3. Process owner

Project manager /Construction Department/Engineering Department

APPROVED BY:			Page 1 of 6
	Name:	Signature:	

አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

4. Definitions & Abbreviations

4.1 Definition

For the purpose of this document in addition to the definition given in ES- ISO 9000:2015 the following definitions are apply

- 4.1.1 **Measured work** = Quantified work executed on the site.
- 4.1.2 **Executed work** = Series of works performed on the site.
- 4.1.3 **Payment certificate** = Prepared document used to request a payment for the execution work on the site.

4.2 Abbreviations

FLW = flow chart

ASER = ASER construction

COD= Construction Department

PM= Project Manager

OP = Operation procedure

IPC= Interim Payment Certificate

OF= Office Engineer

QS= Quantity Surveyor


RE= Resident Engineer

APPROVED BY:	 Name:  Signature:	Page 2 of 6
---------------------	---	-------------


አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

5. Procedure

5.1 process flow chart

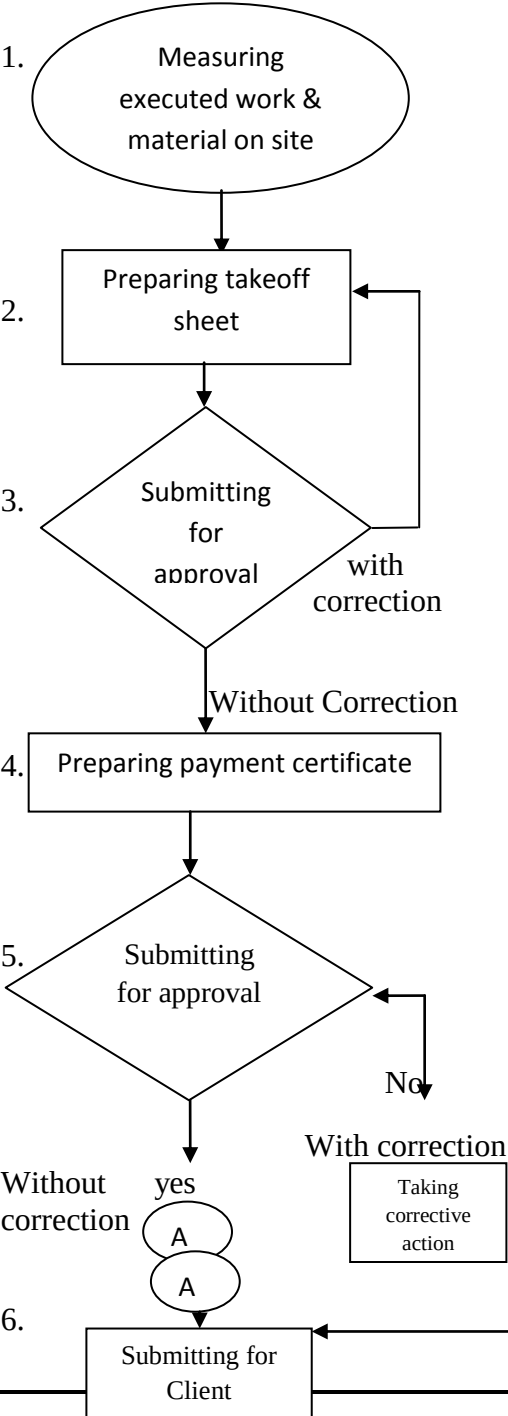Input	Process	Out put	Responsibility
1.Excuted work 2. Measured work & working drawings 3. Prepared takeoff sheet 4. Approved take off sheet 5. Prepared payment certificate 6. Approved payment	 <pre> graph TD A([Measuring executed work & material on site]) --> B[Preparing takeoff sheet] B --> C{Submitting for approval} C -- "with correction" --> B C -- "Without Correction" --> D[Preparing payment certificate] D --> E{Submitting for approval} E -- "No" --> F[Taking corrective action] E -- "yes" --> G([A A]) G --> H[Submitting for Client] </pre>	1.Measured work and material on site 2.Prepared takeoff sheet 3.a.approved take off sheet b. commented take off sheet 4.Prepared payment certificate 5.a.Approved payment b. Corrected payment certificate 6Approved Payment	1. Surveyor 2. OE/QS 3.Office engineer 4.Office engineer 5. PM / COD 6 .Consultant
APPROVED BY:	Name: 	Signature: 	Page 3 of 6

አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

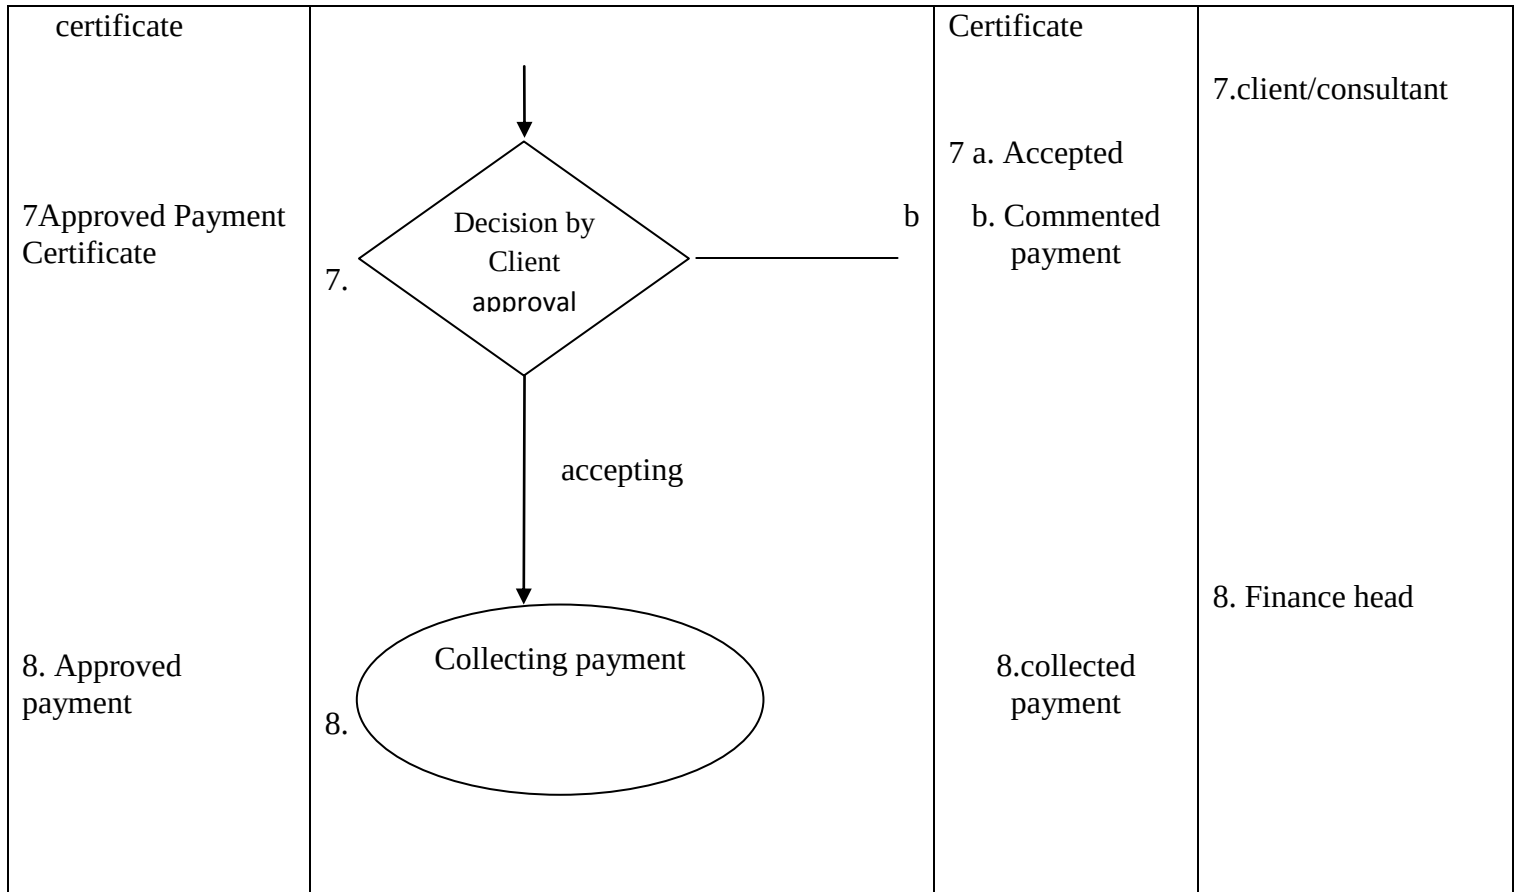

APPROVED BY:	Name:  Signature: 	Page 4 of 6
---------------------	---	-------------

አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

5.2 Description of the process steps

FLW	Process description
1.	After the work is done in accordance of the requirement, specification and passing the required test measuring of work will done jointly with consultant staff .The quantity surveyor/office engineer receives the measured data of executed work from contractor surveyor.
2.	The quantity surveyor /office engineer receives the reviewed data & then prepares the takeoff sheet by using appropriate drawings, specification, take off sheet format, bar schedule format & the collected data etc.
3.	The quantity surveyor/office engineer will submit the takeoff sheet to the QS of consultant with the need of his approval. The QS of consultant reviews the submitted take off sheet carefully by coordinating the takeoff sheet with data on his hand after he will pass two decisions. a. Accepting & signed b. responding with a comment
4.	If the QS of consultant approved the submitted take off sheet, there will be start to payment certificate preparation, if there was comment the quantity surveyor/office engineer takes corrective action & then go to the approval.
5.	After ensuring the accuracy of the payment certificate the project manager will submitted to the consultant office, And then the submitted payment certificate will approved /commented by the consultant office.
6.	After the consultant approved the payment certificate then, the he will forward the approved payment certificate to the client.
7.	The Client will check the approved payment and he will pass a decision a. Commented and the PM or RE will correct it b. approved and pass to his finance department
8.	After the client approved the payment and pass to his finance department the contractor finance department will collect the payment.

6. Records

❖ Measured data

APPROVED BY:	የፕሮጀክት ማስተካከያ Yemane Abreham የፍ. ሥራ ስራ አስፈጻሚ General Manager Name: Signature: 	Page 5 of 6
---------------------	---	-------------

አሰር ኮንስትራክሽን ኃ.የተ.የግ.ማ ASER CONSTRUCTION P.L.C	Procedure	Doc No.
		OP/COD/002
Logo 	Payment Certification & Collection	Issue no
		1

- ❖ Takeoff sheet
- ❖ Payment certificate
- ❖ Approved payment
- ❖ Working drawings

7. Related Documents

Document Title	Document No.
Contract document	

APPROVED BY:			Page 6 of 6
	Name:	Signature:	
